

Development Plan

Universal iOS & Android accessibility app — voice-guided London navigation & NHS portal access

46

Development Days

6 mo

Timeline (2 days/week)


£23,000

Total MVP Cost + VAT

Phase Breakdown

Phase	Days	Weeks	Cost
Phase 0: Foundation & Setup	2	1	£1,000
Phase 1: Voice Engine	5.5	3	£2,750
Phase 2: Navigation Feature	9	4.5	£4,500
Phase 3: NHS Portal (WebView)	10.5	5.5	£5,250
Phase 4: Polish & UX	7.5	4	£3,750
Phase 5: Testing & Launch	11.5	6	£5,750
MVP Total	46	24	£23,000 + VAT

Visual Timeline

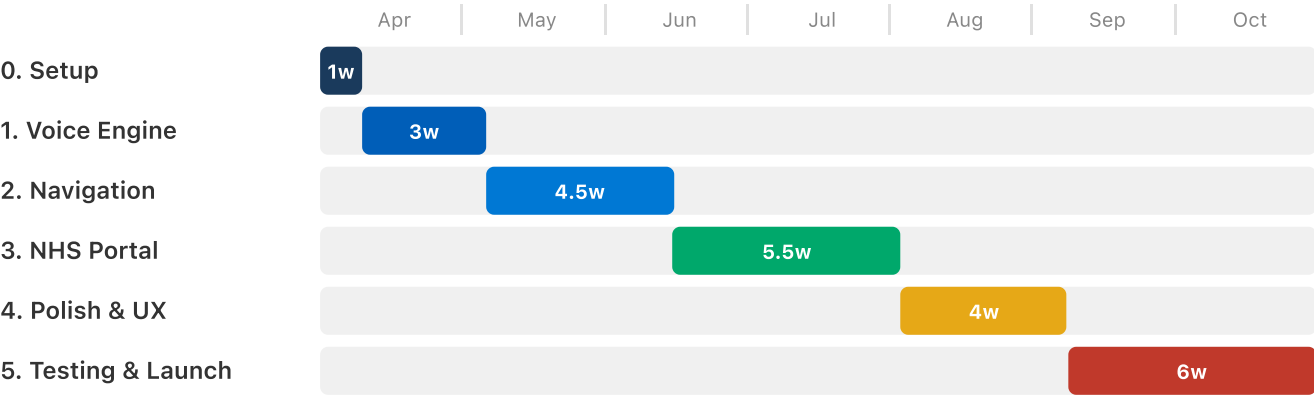

Key Deliverables per Phase

Phase	Deliverables
Phase 0 Foundation	- Expo + TypeScript project scaffold with CI/CD (EAS Build) - Design system: high-contrast themes, large touch targets, semantic markup - Backend API proxy (Node.js) & TfL API registration
Phase 1 Voice Engine	- On-device speech recognition (STT) & text-to-speech (TTS) - Intent parsing: natural language → structured commands - Multi-turn conversation flow & voice command system - Haptic feedback & audio cues
Phase 2 Navigation	- TfL Journey Planner integration with voice-guided step-by-step directions - Transport mode selection via voice (bus, tube, walking) - Favourite destinations ("take me home") & journey history - High-contrast journey display for partially sighted users
Phase 3 NHS Portal	- NHS App website embedded via WebView with voice overlay - Page content extraction & summarisation (read aloud) - Voice commands: "read messages", "request prescription" - NHS Login flow & session management
Phase 4 Polish	- First-launch voice tutorial & onboarding - Settings: speech rate, voice type, contrast, text size - Error handling, offline mode, performance & battery optimisation
Phase 5 Launch	- Automated end-to-end tests - User testing with visually impaired users - App Store & Google Play submission - Documentation & analytics setup

Post-Launch Enhancements (Optional)

Feature	Days	Weeks	Cost
NHS native API integration (replace WebView)	7	3.5	£3,500
GP Connect — Messages	7	3.5	£3,500
EPS — Prescriptions	7	3.5	£3,500

Feature	Days	Weeks	Cost
Advanced conversational voice interface	5	2.5	£2,500
Multi-city UK expansion	7	3.5	£3,500
Post-launch Total	33	17	£16,500 + VAT

Estimated Monthly Running Costs

Service	Monthly Cost
OpenAI API (intent parsing, ~1,000 users)	£30–50
Backend hosting (Railway / Render)	£5–15
Apple Developer Program	£8/mo (£99/yr)
Google Play Developer (one-time £21)	—
TfL API	Free
NHS Login / WebView	Free
Total monthly	~£50–75

Assumptions & Notes

- Day rate: £500/day + VAT
- Working schedule: 2 days per week
- Start date: April 2026 · Target MVP launch: October 2026
- Platform: React Native + Expo (iOS & Android from single codebase)
- NHS integration via WebView MVP — no API onboarding dependency
- Navigation: TfL Journey Planner API (free, London-only for MVP)
- Running costs scale with user count; estimates based on ~1,000 monthly active users
- Post-launch NHS API work is contingent on NHS England onboarding approval
